


ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Qtr 4, 2018		Qtr 1, 2019			Qtr 2, 2019			Qtr 3, 2019			Qtr 4, 2019	
							Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct
1	1.1. Project set up & Assessment	11 days	Fri 23/11/18	Fri 07/12/18															
2	1.1 PM & ISO systems set up	11 days	Fri 23/11/18	Fri 07/12/18		Tom Boylan													
3	1.2 Economic Assessment	136 days	Mon 26/11/18	Mon 03/06/19															
4	1.2.1 Selection of preferred package	36 days	Mon 26/11/18	Mon 14/01/19															
5	1.2.2 junction modelling	50 days	Mon 26/11/18	Fri 01/02/19		Bob Roth													
6	1.2.3 TUBA analysis & Economic Report	40 days	Mon 04/02/19	Fri 29/03/19	5	AECOM													
7	1.2.4 Business Case submitted to DfT	45 days	Mon 01/04/19	Fri 31/05/19	6	AECOM													
8	1.2.5 DfT approve outline Business Case	43 days	Mon 03/06/19	Wed 31/07/19	7	DfT													
9	2 Detailed Design	257 days	Mon 07/01/19	Tue 31/12/19															
10	2.1 Highway Design	257 days	Mon 07/01/19	Tue 31/12/19		John Patchett													
11	2.2 Signals	87 days	Mon 02/09/19	Tue 31/12/19		Chris Ashton													
12	2.3 Landscaping	109 days	Thu 01/08/19	Tue 31/12/19		Cathy Gillespie													
13	3 Land & Legal	613 days	Mon 26/11/18	Wed 31/03/21															
14	3.1 Appoint Weighmans (Legal)	10 days	Mon 03/12/18	Fri 14/12/18		Tom Boylan													
15	3.2 Appoint Bruton Knowles (Property)	10 days	Mon 03/12/18	Fri 14/12/18		Tom Boylan													
16	3.3 Land Registry and valuations	60 days	Mon 17/12/18	Fri 08/03/19	15	Bruton Knowles													
17	3.4 Commence negotiations (3rd party lan	539 days	Fri 08/03/19	Wed 31/03/21	16	Bruton Knowles													
18	4 Environmental Assessments	261 days	Tue 01/01/19	Tue 31/12/19															
19	4.1 Hydrology Assessment	261 days	Tue 01/01/19	Tue 31/12/19		AECOM													
20	4.2 Ecology	86 days	Tue 01/01/19	Tue 30/04/19		Baker Consultants													
21	4.3 Ground Investigation	88 days	Mon 01/04/19	Wed 31/07/19		Cathy Gillespie													
22	4.4 Noise assessments	152 days	Mon 01/04/19	Tue 29/10/19	6	Dave Collins													
23	5 Consultation	544 days	Mon 03/12/18	Thu 31/12/20															
24	5.1 Public Consultation	43 days	Mon 03/06/19	Wed 31/07/19		David Pick & Tom													
25	5.2 Engage with EA	282 days	Mon 03/12/18	Tue 31/12/19		Tom Boylan													
26	5.3 District, Town & Parish Councils	414 days	Mon 03/06/19	Thu 31/12/20		Tom Boylan													
27	5.4 Engage with Natural England	85 days	Mon 03/12/18	Fri 29/03/19		Tom Boylan													
28	5.5 TRO consultation	154 days	Mon 01/06/20	Thu 31/12/20		Jeff Burton													
29	6 Planning	174 days	Thu 01/08/19	Tue 31/03/20															
30	6.1 Writing of planning application	97 days	Thu 01/08/19	Fri 13/12/19		Tom Boylan													
31	6.2 Submission of application	1 day	Fri 13/12/19	Fri 13/12/19		Tom Boylan													
32	6.3 Planning determined	65 days	Mon 16/12/19	Fri 13/03/20		NCC Planners													
33	7 CPO & SRO	325 days	Sat 30/11/19	Sat 27/02/21	32														
34	7.1 Writing of Orders (inc. NCC approvals)	76 days	Sat 30/11/19	Fri 13/03/20		Via & Weightmans													
35	7.2 Making of Orders	12 days	Mon 16/03/20	Tue 31/03/20		Via & Weightmans													
36	7.3 Notification & Publication	43 days	Wed 01/04/20	Fri 29/05/20		Via & Weightmans													
37	7.4 Relevant Date	26 days	Fri 29/05/20	Fri 03/07/20		DfT													
38	7.5 Public Inquiry	26 days	Fri 23/10/20	Fri 27/11/20		DfT													
39	7.6 Decision	27 days	Sat 23/01/21	Sat 27/02/21		DfT													
40	8 DfT Full Approval	61 days	Thu 19/12/19	Thu 12/03/20															
41	8.1 Writing of Full Approval document	30 days	Thu 19/12/19	Wed 29/01/20		David Pick/Tom Bc													
42	8.2 Full Approval Submission	1 day	Thu 30/01/20	Thu 30/01/20	41	David Pick													
43	8.3 DfT sign off	30 days	Fri 31/01/20	Thu 12/03/20	42	DfT													
44	9 Procurement	44 days	Mon 01/02/21	Thu 01/04/21	29,39	Mike Barnett													

Project: A614v2may19.mpp
Date: Thu 30/05/19

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
Summary		Inactive Task		Duration-only		Finish-only			





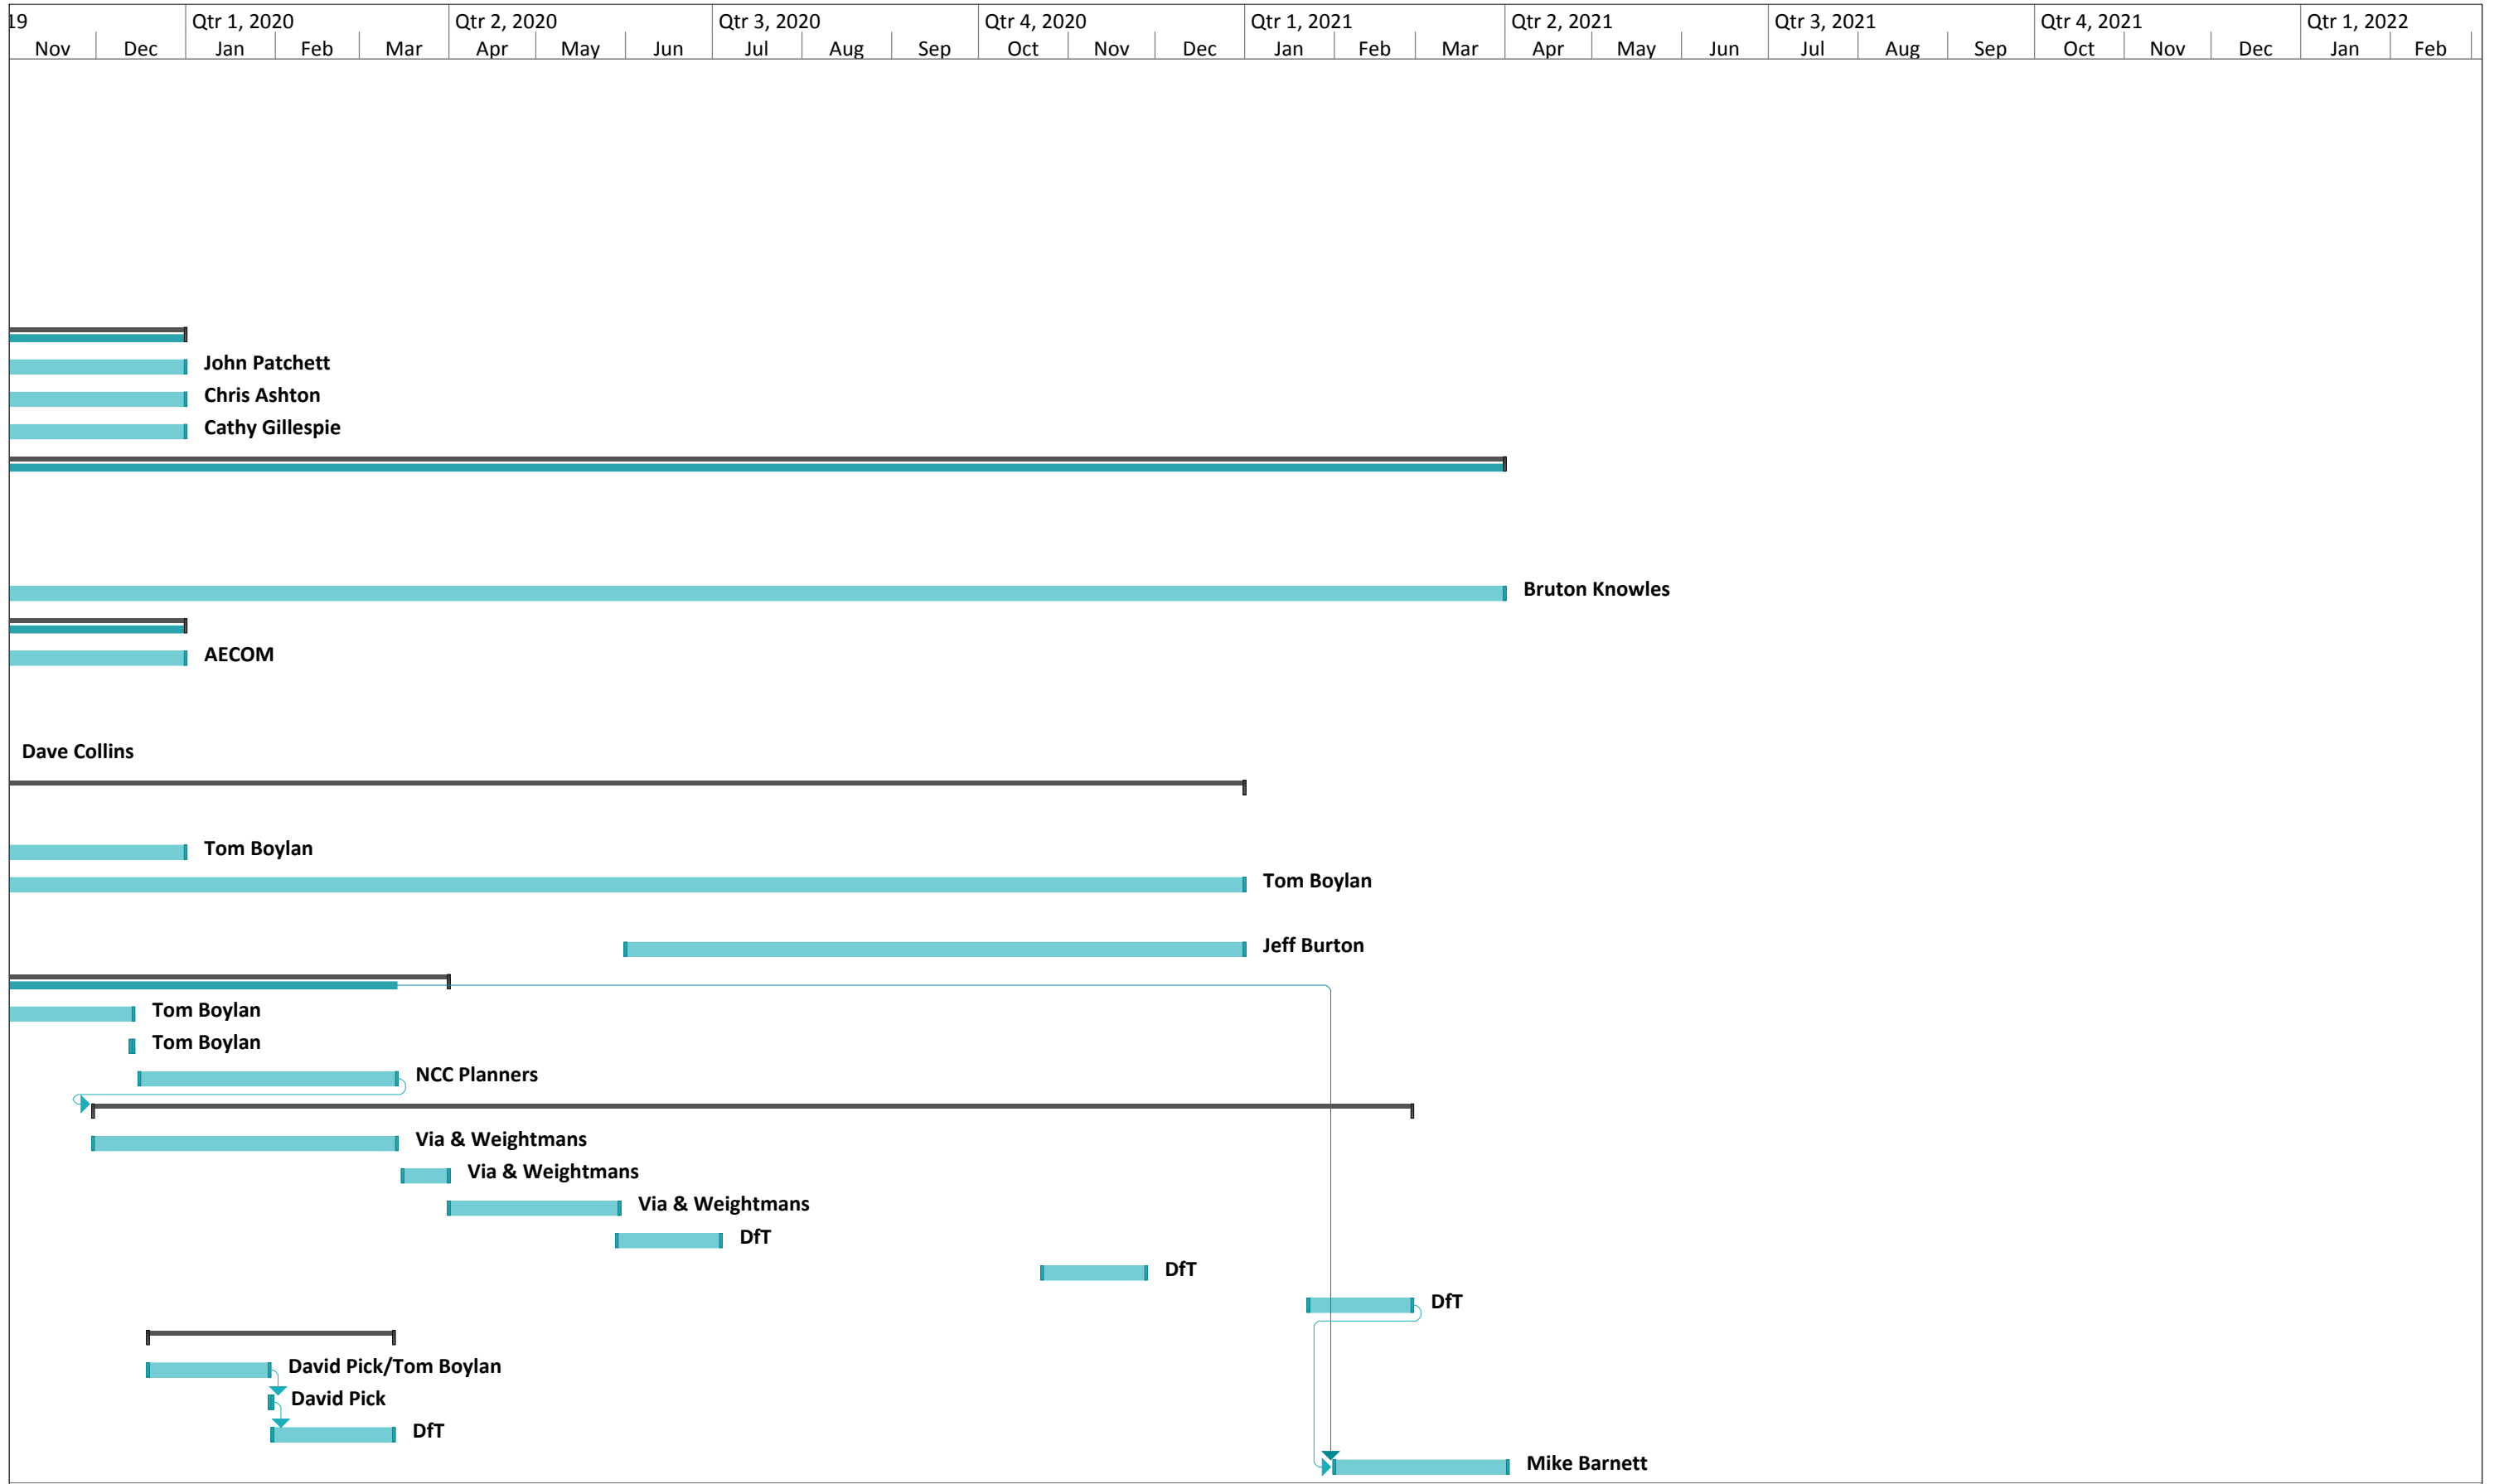














ID	Task Mo	Task Name	Duration	Start	Finish	Predeces	Resource Names	Qtr 4, 2018			Qtr 1, 2019			Qtr 2, 2019			Qtr 3, 2019			Qtr 4, 2019	
								Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov
45	★	10 Construction	847 days	Thu 01/04/21	Fri 28/06/24		TBC														

Project: A614v2may19.mpp Date: Thu 30/05/19	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
	Summary		Inactive Task		Duration-only		Finish-only			



Project: A614v2may19.mpp Date: Thu 30/05/19	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
	Summary		Inactive Task		Duration-only		Finish-only			

Project: A614v2may19.mpp
Date: Thu 30/05/19


Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
Summary		Inactive Task		Duration-only		Finish-only			



Project: A614v2may19.mpp
Date: Thu 30/05/19

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
Summary		Inactive Task		Duration-only		Finish-only			

	Qtr 2, 2022				Qtr 3, 2022			Qtr 4, 2022			Qtr 1, 2023			Qtr 2, 2023			Qtr 3, 2023			Qtr 4, 2023			Qtr 1, 2024			Qtr 2, 2024		
Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	



Project: A614v2may19.mpp Date: Thu 30/05/19	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
	Summary		Inactive Task		Duration-only		Finish-only			
